

PG&E Gas Operations & Technical Training Center

Winters, CA

Project Report – July 2016



Safety

- Daily Safety meetings have been reoccurring at the beginning of shifts daily.

DPR & Subcontractor Work Hours to Date	28,095
Accidents	0



Planned Activities for June/July 2016

Learning Center / M&C		33	07-Jul-16 A	24-Aug-16	5.71%
Learning Center / M&C Structure		33	07-Jul-16 A	24-Aug-16	5.71%
Learning Center / M&C Area 1&2		7	11-Jul-16	19-Jul-16	0%
Crete633	Place and Finish Slab On Grade / Casting Pads / Saw Cut	4	11-Jul-16	14-Jul-16	0%
Crete641	Strip / Clean SOG Edge Forms	5	13-Jul-16	19-Jul-16	0%
Learning Center Area 1&2 Slab Depressions		11	18-Jul-16	01-Aug-16	0%
Crete330	Strip Laser Foam Area 1&2 Slab Depressions	5	18-Jul-16	22-Jul-16	0%
Crete340	Install Area 1&2 Depressed Slab Edge Forms	3	25-Jul-16	27-Jul-16	0%
Crete360	Set Floor Drains / Plumbing Blockouts	2	28-Jul-16	29-Jul-16	0%
Learning Center / M&C Area 3		31	07-Jul-16 A	22-Aug-16	6.06%
Crete721	Install Area 3 Trough Slab Forms	2	07-Jul-16 A	12-Jul-16	33.33%
Crete731	Install Area 3 Trough Slab / Wall Concrete Reinforcing	2	13-Jul-16	14-Jul-16	0%
Crete761	Place / Finish Trough Slabs	1	18-Jul-16	18-Jul-16	0%
Crete771	Strip Trough Slab Forms	1	19-Jul-16	19-Jul-16	0%
Crete741	Install Trough Wall Forms	10	20-Jul-16	02-Aug-16	0%
Crete781	Place & Finish Trough Walls	3	03-Aug-16	05-Aug-16	0%
Crete751	Strip Clean Area 3 Trough Wall Forms	3	08-Aug-16	10-Aug-16	0%
Crete748	Lean Mix Backfill	1	11-Aug-16	11-Aug-16	0%
T&D Tech Center		38	29-Jun-16 A	31-Aug-16	15.56%
T&D Structure		38	29-Jun-16 A	31-Aug-16	15.56%
TD2510	Strip / Clean Cure Concrete Slab	14	29-Jun-16 A	28-Jul-16	33.33%
TD2510	Concrete Curbs Reinforcing / Form Place and Finish	7	14-Jul-16	22-Jul-16	0%
TD1110	Erect Structural Steel / Z Girts & Purlins	7	29-Jul-16	08-Aug-16	0%
TD2490	Install Roof Panels Mechanical Curbs	7	09-Aug-16	17-Aug-16	0%
TDFRM10	Frame Interior Walls at 3 and 9 Line	3	15-Aug-16	17-Aug-16	0%
Utility Village / Transmission / Crane Certification		33	06-Jul-16 A	24-Aug-16	8.33%
Transmission		33	06-Jul-16 A	24-Aug-16	8.33%
Con2280	Install Concrete Footing/ Wall Dowel Reinforcing	1	06-Jul-16 A	11-Jul-16	66.67%
Con2290	Place and Finish Concrete Footings	2	13-Jul-16	14-Jul-16	0%
Con2300	Form / Place and Finish Concrete Walls	15	15-Jul-16	04-Aug-16	0%



Progress Photos



Bike Path, PG&E One Way and West Parking Lot Paving





T&D Building Edge Form,
Rock, Vapor Barrier and Slab
Reinforcing (Facing South)

T&D Building Slab Poured (Facing
South)




T&D Building Slab
(Facing South)



Learning Center Area 1 Edge Form, Rock, Vapor Barrier and Slab Reinforcing (Facing East)



Learning Center Area 2 Edge Form, Rock, Vapor Barrier and Slab Reinforcing (Facing West)

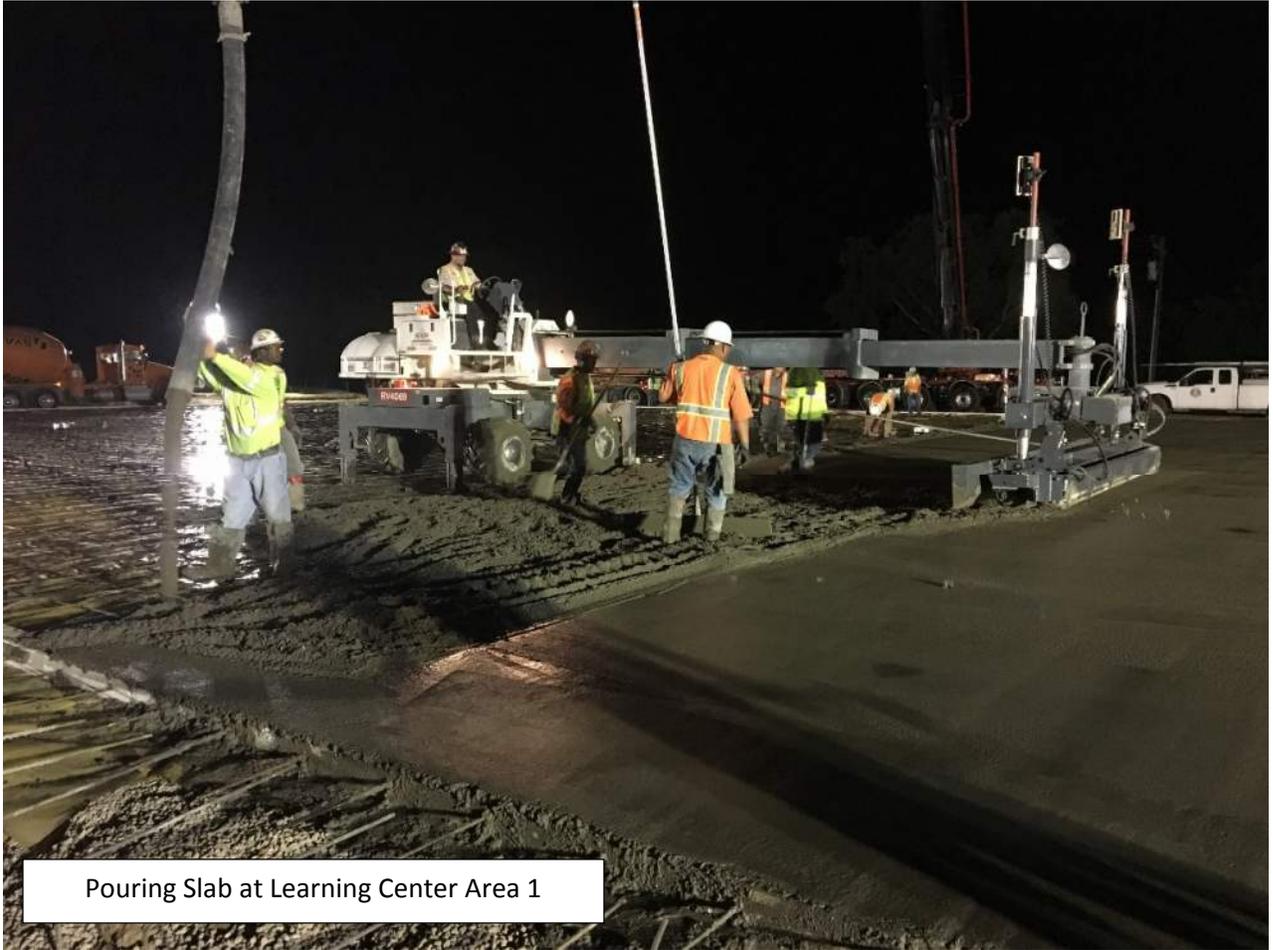

Pouring Slab at Learning Center Area 1



Finishing Learning Center Area 1 Slab





Learning Center Area 1 Slab (Facing West)





Pouring Tilt Panel Casting Pads Around Perimeter of Learning Center



Finished Tilt Panel Casting Pads Around Perimeter of Learning Center





East and West Cold Pit Concrete Reinforcing (Facing West)



East and West Cold Pits Footings Poured (Facing West)

Learning Center Area 3
Flow Lab East Trough, Slab
Forming and Reinforcing
(Facing South)



Learning Center Area 3
Flow Lab Center Trough,
Slab Forming and
Reinforcing (Facing South)

Learning Center Area 3
Flow Lab West Trough, Slab
Forming and Reinforcing
(Facing South)



West Proto II Sound Wall
(Facing South)



Contact: Ian Bolnik DPR Construction Project Manager 916-568-3434 ianB@dpr.com *Scope and bid related questions	Contact: Bill Hill DPR Construction Superintendent 916-568-3434 billhi@dpr.com *Safety/Logistics/Schedule questions
---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------	---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------

